




NOTES:

1. TOTAL CUT VOLUME 118,000m³.
2. TOTAL FILL VOLUME 83,000m³.
3. TOTAL EARTHWORKS AREA 114,000m².
4. EARTHWORKS SHOWN IN BULK VOLUMES ONLY (NEAREST 1m).
5. GOLF COURSE ROUTING AND LEVELS BY DARIUS OLIVER, PLANET GOLF.
6. FINAL DESIGN LEVELS AND EARTHWORK EXTENTS TO BE DETERMINED AT THE TIME OF CONSTRUCTION.
7. CUT/FILLS TO BE CERTIFIED BY ENGINEER
8. SEDIMENT CONTROL MEASURES TO BE AS PER "EROSION AND SEDIMENT CONTROL GUIDELINES FOR THE WELLINGTON REGION".
9. SITE TO BE PROGRESSIVELY STABILISED AS WORK PROCEEDS WITH TOPSOIL, MULCHING AND GRASS COVER.
10. FAIRWAY AND GREENS WILL BE CONSTRUCTED IN ACCORDANCE WITH THE MAHI TAHI CONSTRUCTION PROCESS DATED 1ST DECEMBER, 2020.
11. VOLUMES CALCULATED BETWEEN EXISTING SURFACE

AND PROPOSED SURFACE.
 12. AREAS 11 AND 12 FROM THE BML REPORT ARE NATURAL WETLANDS. NO EARTHWORKS ARE TO OCCUR WITHIN 10m OF THESE AREAS. EARTHWORKS WITHIN 100m WILL RESULT OR LIKELY TO RESULT IN COMPLETE OR PARTIAL DRAINAGE OF ALL OR PART OF THE NATURAL WETLAND.

LEGEND:

-  CONSTRUCTION NO GO AREA
-  EARTHWORKS EXTENT
-  SILT FENCE
-  BUND

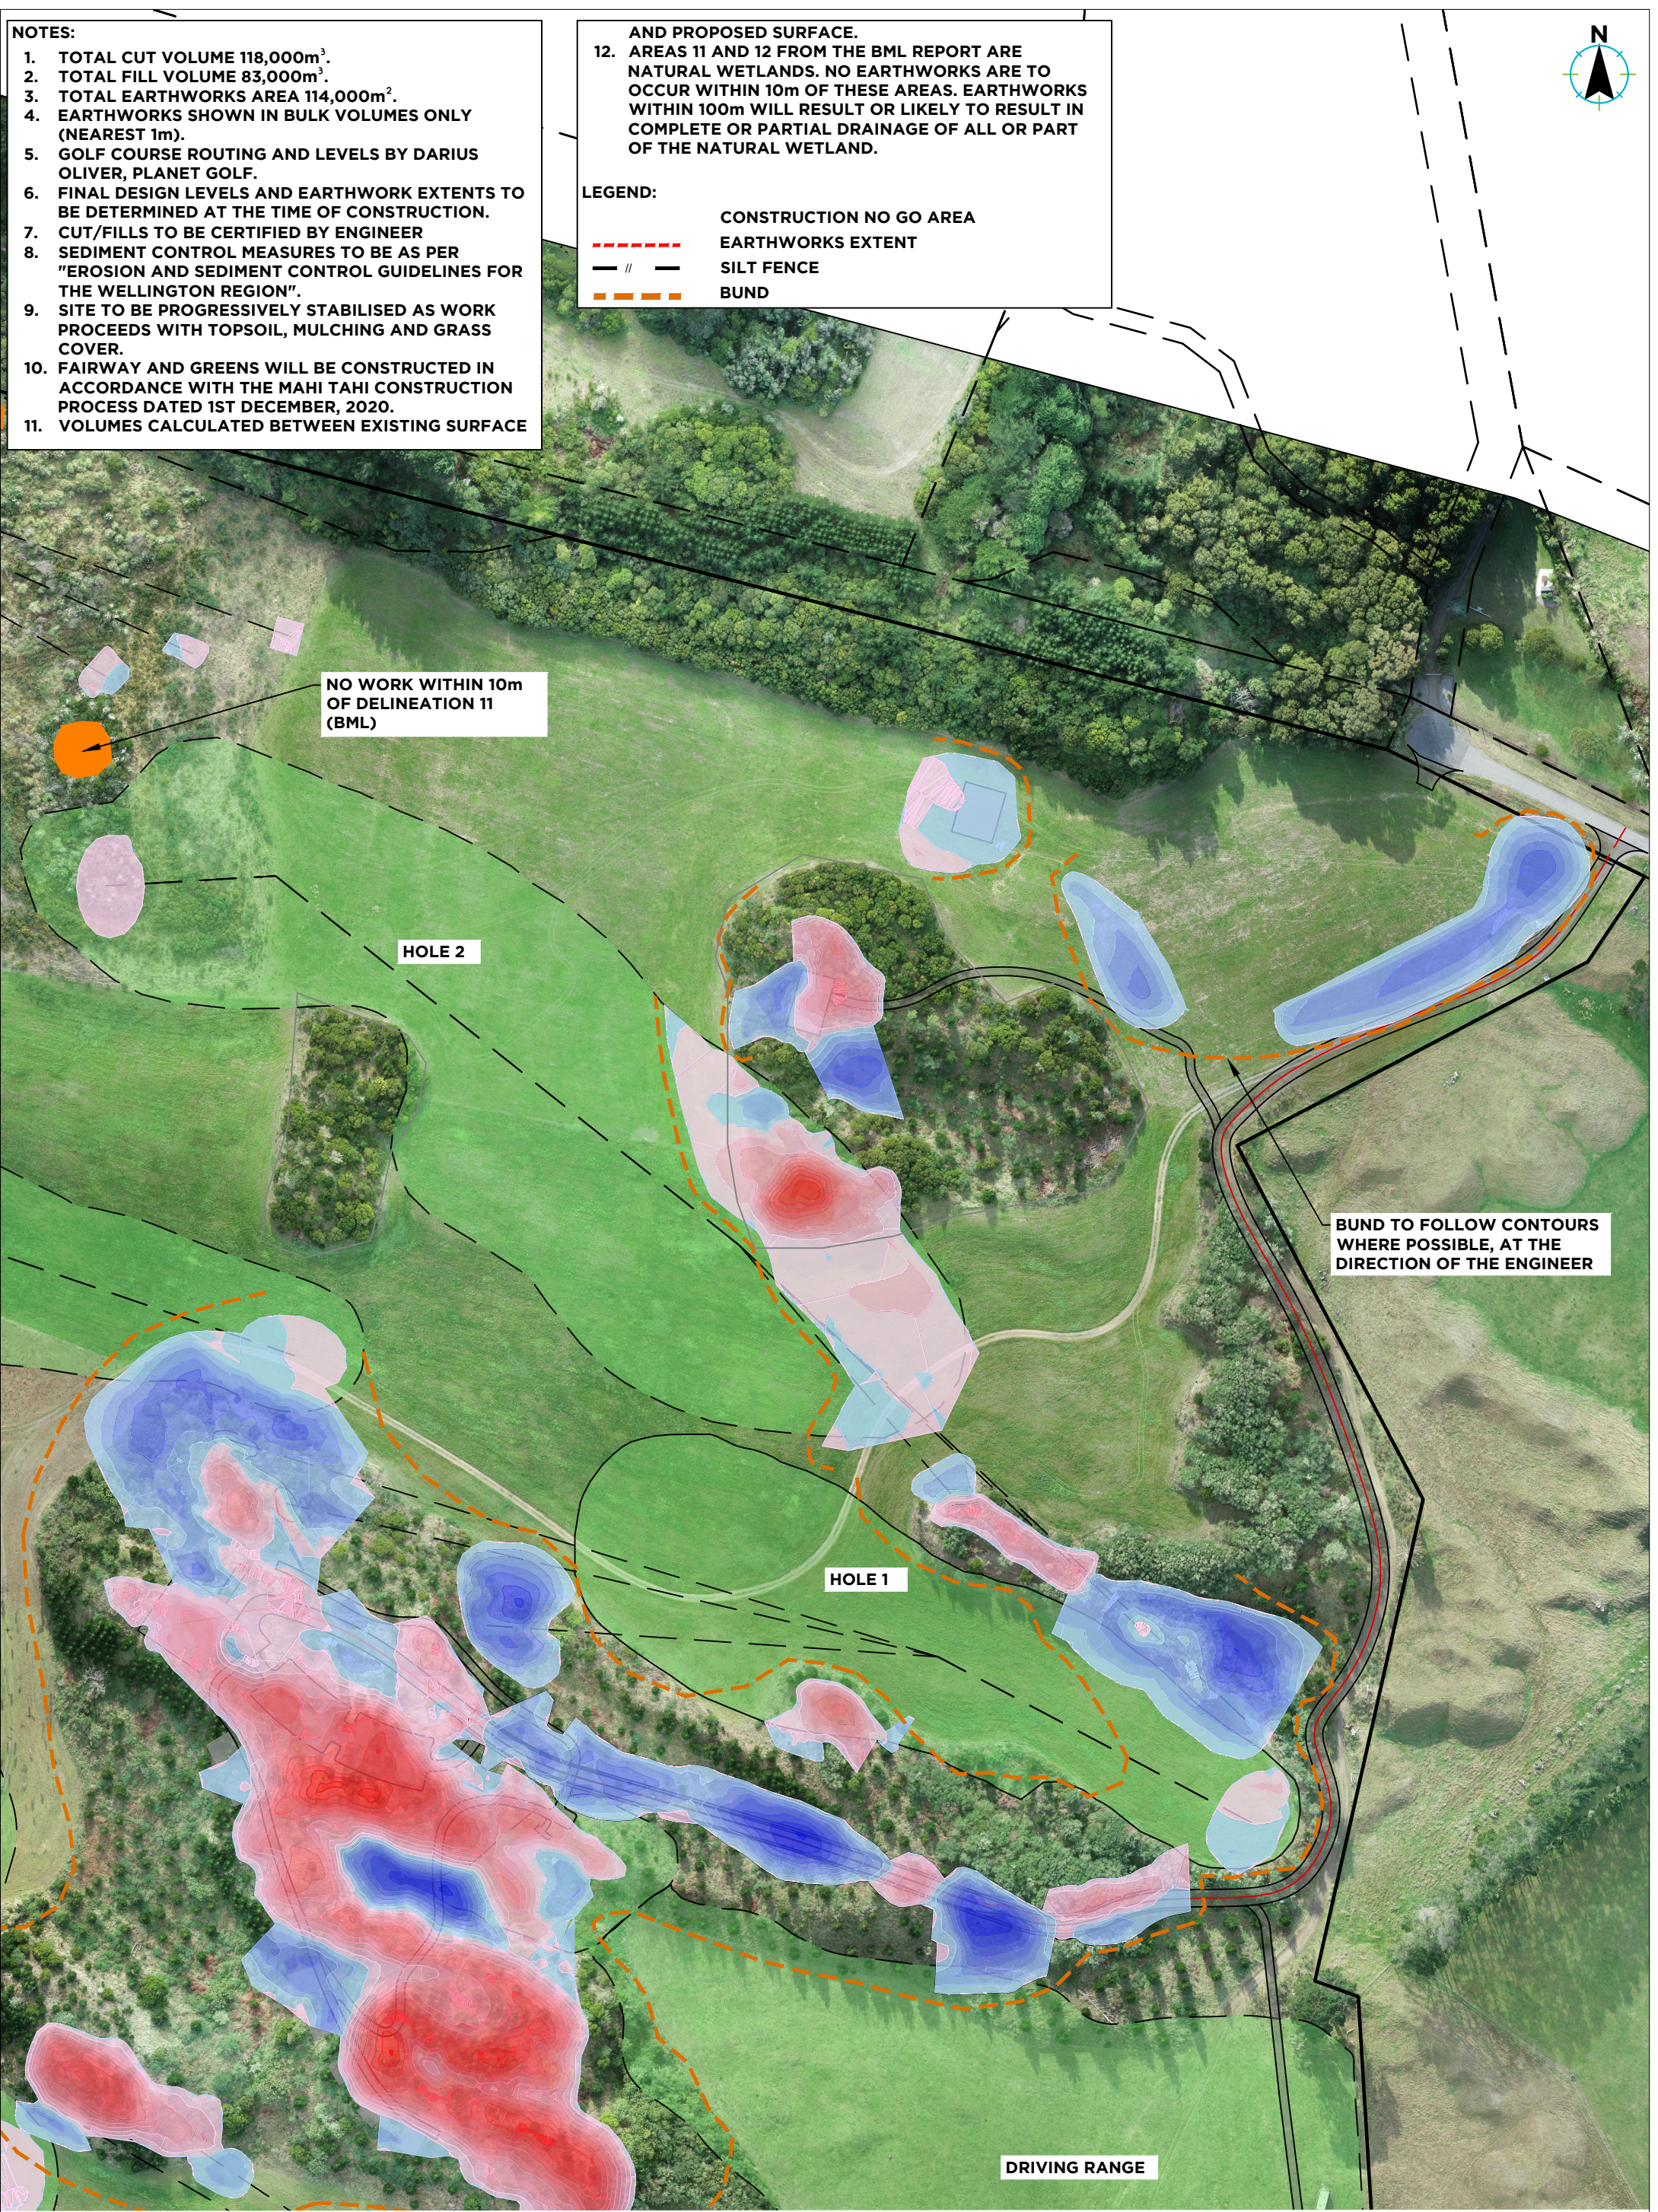

NO WORK WITHIN 10m OF DELINEATION 11 (BML)

HOLE 2

HOLE 1

BUND TO FOLLOW CONTOURS WHERE POSSIBLE, AT THE DIRECTION OF THE ENGINEER

DRIVING RANGE

PREPARED BY  LANDMATTERS	CLIENT GRENADIER DEVELOPMENTS LIMITED	PROJECT DOUGLAS LINKS - OHAU	DRAWING TITLE ESCP PLAN NORTH EAST CORNER	DATE 15/06/21	PROJECT NO. 709
					SCALE 1:1000 @ A1 1:2000 @ A3
					DRAWING NO. J709-ENG-151
